


Project: Åby Nordgård dränerin Date: 2017-01-25	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

ID	% Work Comple	Task Name	Duration	Start	Finish		Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
97	0%	Möte	2 hrs	2017-01-26	2017-01-26																				
98	0%	FÄ insats	6 days	2017-01-27	2017-02-05																				
99	0%	RöjTeam	10 days	2017-01-27	2017-02-10																				
100	0%	Gräv och dränera	22 days	2017-02-01	2017-03-03																				
101	0%	Färdig länga	2 hrs	2017-03-03	2017-03-03																				
102																									
103	0%	Trav 2 (10st)	51 days	2017-01-20	2017-04-03																				
104	0%	Brev	2 hrs	2017-01-20	2017-01-23																				
105	0%	Dokumentation	3 days	2017-01-23	2017-01-25																				
106	0%	Möte	2 hrs	2017-02-05	2017-02-05																				
107	0%	FÄ insats	5 days	2017-02-15	2017-02-22																				
108	0%	RöjTeam	10 days	2017-02-20	2017-03-06																				
109	0%	Gräv och dränera	22 days	2017-03-02	2017-04-03																				
110	0%	Färdig länga	2 hrs	2017-04-03	2017-04-03																				
111																									
112	0%	Trav 4 (11st)	55 days	2017-01-20	2017-04-07																				
113	0%	Brev	2 hrs	2017-01-20	2017-01-23																				
114	0%	Dokumentation	3 days	2017-01-23	2017-01-25																				
115	0%	Möte	2 hrs	2017-02-05	2017-02-05																				
116	0%	FÄ insats	5 days	2017-02-15	2017-02-22																				
117	0%	RöjTeam	11 days	2017-02-20	2017-03-07																				
118	0%	Gräv och dränera	25 days	2017-03-03	2017-04-07																				
119	0%	Färdig länga	2 hrs	2017-04-07	2017-04-07																				
120	0%																								
121	0%	Måldomargatan	94 days	2017-02-24	2017-08-10																				
130																									
139																									
148																									

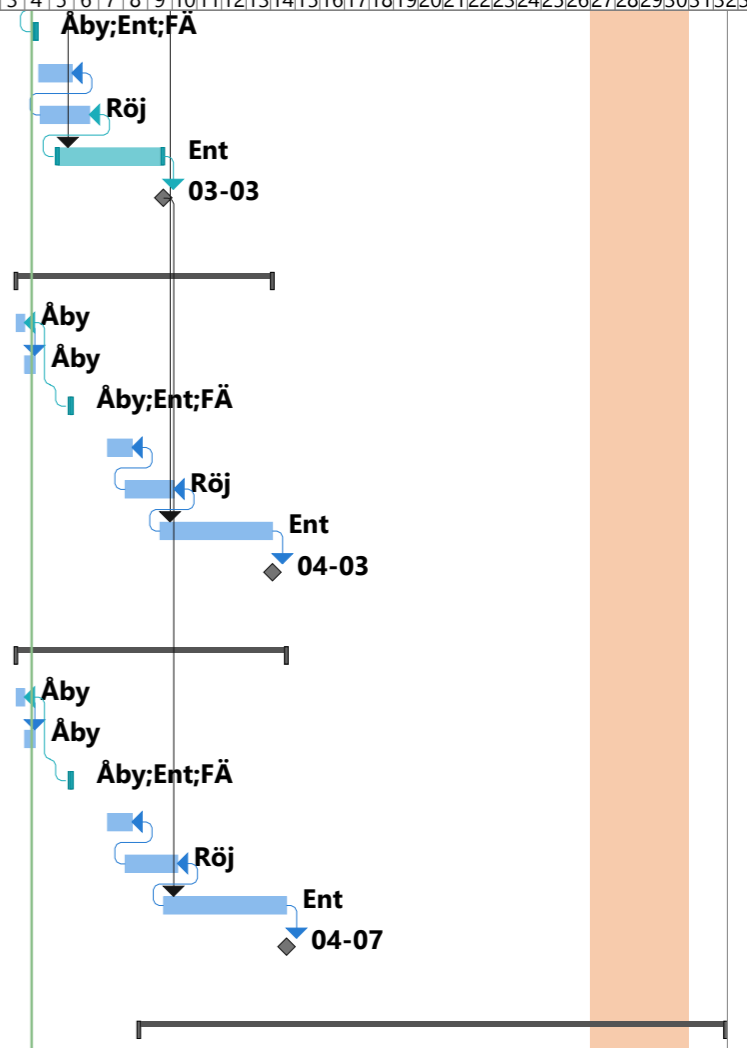

Project: Åby Nordgård dränerin
Date: 2017-01-25

Task		Project Summary		Manual Task		Start-only		Deadline
Split		Inactive Task		Duration-only		Finish-only		Progress
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress
Summary		Inactive Summary		Manual Summary		External Milestone		
